

REPUBLIC OF IRAQ

MINISTRY OF PLANNING

**Iraq “Social Fund for Development” Project
(SFDP)**

**ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN
(ESMP)**

**FOR THE
INSTALLATION
OF**

**WATER DISTRIBUTION NETWORK IN SIX VILLAGES (ABU
KANBARA, ABU SARIFAH, AL AKSHEH, AL THAWIHER,
FINJAN AL THAHER AND AL TAWAWREH)
IN
AL-MUTHANNA GOVERNORATE**

18TH JANUARY 2020

Table of Contents

Executive Summary	1
1. INTRODUCTION	4
2. PROJECT DESCRIPTION	4
2.1 Objective of the Works	5
2.2 Scope of Work.....	5
2.3 Contractors Camp and Storage of Equipment	7
3. BASELINE CONDITIONS	7
3.1 The Project Area.....	7
3.2 Environmental and Social Baseline Conditions.....	8
3.2.1 Climate	8
3.2.2 Air Quality	8
3.2.3 Site Topography and location	8
3.2.4 Land use	8
3.2.5 Flooding.....	8
3.2.6 Noise	8
3.2.7 Heritage Environment.....	8
3.2.8 Traffic Level	9
3.2.9 Land acquisition	9
3.2.10 Social Aspects.....	9
4. LEGAL ASPECTS	9
4.1 Iraqi environmental legislations.....	9
4.2 The World Bank Safeguards Policies.....	10
4.3 WBG EHS: The Environmental, Health, and Safety (EHS) Guidelines	11
5. IMPACT ASSESSMENT AND MITIGATION MEASURES	11
5.1 Construction Phase	11
5.2 Operational Phase.....	11
6. ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN	12
7. ENVIRONMENTAL AND SOCIAL MONITORING PLAN	22
7.1 Environmental and Social Monitoring	22
7.2 ESMP Institutional Arrangements.....	22
7.3 Reporting requirements.....	22
7.4 Capacity Development and Resources Requirements.....	25
8. PUBLIC CONSULTATION	26

8.1 Consultation Process:.....	26
8.2 Consultation Results:.....	26
9. Grievance Redress Mechanism.....	27
ANNEXES	28
Annex 1: Public Consultations Photos	28
Annex (2): Sample of Public Consultation at these six Villages	29
Annex (3): Sample individual interviews for both men and women	32

List of Figures

Figure 1: location of the six villages (google earth).....	5
Figure 2 Map of Iraq on the right and Al-Muthannagovernorate on the left.	7

List of Tables

Table 1: Information about the villages.....	7
Table 2: Applicable Laws and Regulations in Iraq	10
Table 3: Summary of Impact Assessment during Construction	11
Table 4: Mitigation Measures during Construction Phase.	13
Table 5: Mitigation Measures during Operation Phase.	21
Table 6: Monitoring Activities during Construction Phase.	23
Table 7: Capacity Development Requirements.....	25
Table 8: Contact Information for GRM	27

List of Abbreviations

CDGs	Community Development Groups
ESMP	Environmental and Social Management Plan
EHS	Environmental, Health, and Safety
ESMF	Environmental and Social Management Framework
GIIP	Good International Industry Practice
GOI	Government of Iraq
GRM	Grievance Redress Mechanism
GBV	Gender Based Violence
MOE	Ministry of Environment
MOP	Ministry of Planning
MSDS	Material Safety Data Sheets
OP	Operational Policy
PAPs:	Project Affected Peoples
PMO	Project Manager Office
PPE	Personal Protective Equipment
RE	Resident Engineer
SFD	Social Fund Development
WB	World Bank
WHO	World Health Organization

EXECUTIVE SUMMARY

INTRODUCTION	<p>This ESMP is prepared in accordance to the ESMF requirements of the SFD project. The main objective of the ESMP is to assess the environmental and socio-economic impacts of the subprojects (during construction and operation phases) and to propose mitigation measures to mitigate the impacts associated with subproject. This subproject includes the installation of water distribution network in six villages in Al-Muthanna governorate. These water networks are expected to result in significant socio-economic benefits for the local communities and surrounding areas as it will provide potable water to these villages which does not have a water distribution network and therefore it will protect public health. Also ensure the incoming water quality that was produced in water treatment plant to the consumers, and supply water equitably to the consumers with sufficient pressure in the area.</p>	
PROJECT DESCRIPTION	<p>The subproject consists of upgrading and installation of 33.75 Km of water networks in 6 villages. The 6 villages are: Abu Kanbara, Abu Sarifah, Al Aksheh, Al Thawiher, Finjan Al Thaher and Al Tawawreh village, in Al-Muthanna governorate. The upgrading and installation will need about 15-20 worker per day for each site. Workers are expected to be hired locally, however if a construction camp is deemed necessary, it will be installed on vacant state-owned land. Also, equipment and construction materials will be stored on vacant state-owned land. The anticipated duration of all works is around 180 days for all the water networks including mobilization and demobilization of contractor.</p>	
ENVIRONMENTAL AND SOCIAL BASELINE CONDITIONS	Climate	<p>Al-Muthanna governorate is located in the southern part of Iraq, which has an arid climate. The major rain, is about 106 mm yearly, falls during the period December thru March, with a spread showering in April. The average annual temperature is 23.8 °C. The average monthly wind velocity is 2.3m/s.</p>
	Air quality	<p>The ambient air quality is within normal range.</p>
	Land	<p>No additional land for the work is needed to proceed with these roads.</p>
	Biodiversity	<p>No protected areas or endangered species (there is no critical or high biodiversity values that might be affected) in the vicinity of the sites.</p>

	Culture heritage	The sites adjacent areas do not include any historical or cultural sites.
POLICY AND LEAGAL FRAMEWORK	Applicable Iraqi laws	
	<ul style="list-style-type: none"> • Law no. 37 of 2008 MoE roles and responsibilities. • Law no. 27 of 2009 Protection of Environment • Regulation 2 of 2001 Preserving water resources • Law No.3,1997 Environment protection • Law No. 55. 2002 Heritage and antiques 	Applicable WB Policies
ENVIRONMENTAL AND SOCIAL IMPACT ANALYSIS	• Environmental Receptor	
	Air Quality	Medium
	Noise	Medium
	Water Resources	Low
	Soil	Low
	Solid and hazardous wastes	Low
	Flora & Fauna	Not significant
	Topography and landforms	Not significant
	Impacts on local traffic	Not significant
	Health and Safety	High
	Socio-Economic impacts	Low
	Child Labor	Medium
PUBLIC CONSULTATION RESULTS	Two modalities of consultations were carried out for this subproject. Public consultation was conducted in all 6 villages with men only due to the tribes' habit where 64 participants attended. The second approach was one-to-one interviews with both men and women to have their views and concerns of potential impacts during implementation. The number of individuals interviewed was 8 women and 30 men.	
GRIEVANCE REDRESS MECHANISM	The SFD is in the process of establishing a free hotline and is expected to be functioning within the next few months. Meanwhile, in order to comply with the WB requirements, SFD has temporary assigned three staffs as focal points with their cell phone numbers to be disseminated at each road site for receiving calls and handling complaints. The contact details will be posted at site signboard and the complaint boxes will be installed in each location.	

Main Report

1. INTRODUCTION

According to the Environmental and Social Management Framework (ESMF) which was prepared for the Social Fund for Development project (SFDP) and disclosed locally and on the WB website, an Environmental and Social Management Plan (ESMP) should be prepared, cleared and publically consulted upon and disclosed prior to the commencement of any construction activities for all the subproject's components.

This ESMP was developed to identify, assess and mitigate the environmental and social risks and impacts associated with the installation of water networks of about 33.75 km long in six villages. These water networks are located in the following villages: **Abu Kanbara, Abu Sarifah, Al Aksheh, Al Thawiher, Finjan Al Thaher and Al Tawawreh** within Al-Muthanna governorate.

The ESMP was prepared by an independent consultant according to requirements of the World Bank (OP 4.01), and Iraqi regulations. The ESMP should be implemented by all relevant parties.

The objectives of this ESMP are to:

- Provide practical and achievable actions to ensure that the subprojects adverse environmental and social impacts are properly avoided or mitigated.
- Illustrate the institutional arrangements for implementing and monitoring the mitigation actions
- Integrate community views and input on the environmental and social impacts of these subprojects
- Comply with WB and national requirements
- Provide information to the local community on the subprojects activities, the associated risks and impacts, mitigation measures and Grievance Redress Mechanism (GRM) system.

2. PROJECT DESCRIPTION

These subprojects involve the upgrading of water distribution networks for six villages for a total length of 33.75 km located in the Governorate of Al-MuthannaSoutheast of Iraq. These water networks will serve **Abu Kanbara, Abu Sarifah, Al Aksheh, Al Thawiher, Finjan Al Thaher and Al Tawawreh** villages. Most of these villages suffer from the deterioration of the infrastructure as there are no water distribution networks in these villages and they purchasing water in bottles or in water tankers to achieve their daily requirements. The locations of these water networks are shown in the figure below:

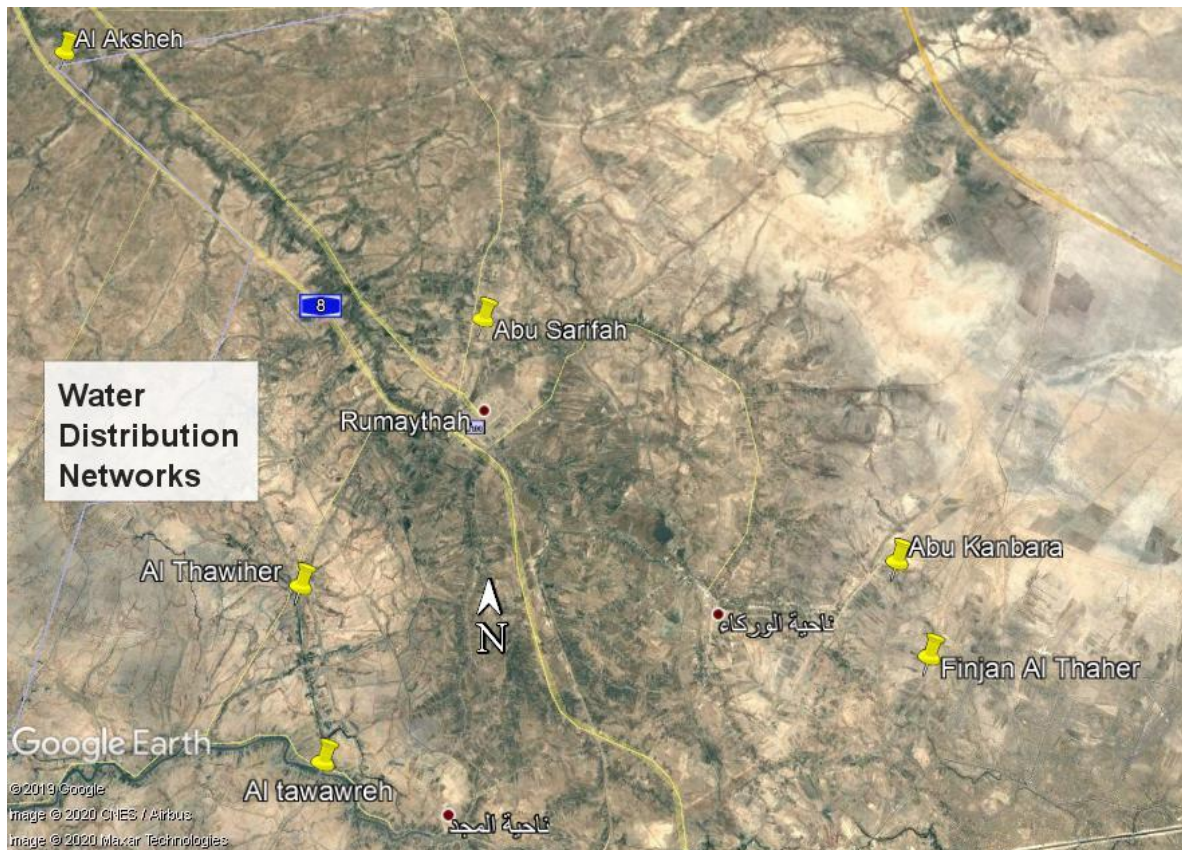


Figure 1: location of the six villages (google earth)

2.1 Objective of the Works

The objective of this subproject is to install water distribution networks for six villages. These water networks are expected to result in significant socio-economic benefits for the local communities and surrounding areas as it will provide potable water to these villages which does not have a water distribution network and therefore it will protect public health. Also ensure the incoming water quality that was produced in water treatment plant to the consumers, and supply water equitably to the consumers with sufficient pressure in the area.

2.2 Scope of Work

The total length of the pipes within the village's network is about 33.75 Km including different diameters ranging from 110-225mm as shown in the table below:

Table 1: Information about the villages

Village	Diameter (mm)	Length (m)
Abu Kanbara	225	3500
	160	1200
Abu Sarifah	225	3500
	110	3000
Al Aksheh	160	2000
	110	8000
Al Thawiher	160	750

	110	700
Finjan Al Thaher	160	600
Al Tawawreh	225	3500
	160	5000
	110	2000
Total		33750

The network will be connected to the existing main potable water pipeline passing by each village that is connecting the nearest water treatment plants. The distribution networks will connect the houses in the villages to the main water pipeline. The installation works will include the following activities:

1. Providing the necessary materials and equipment for excavating trenches at a depth of 120 cm and a width of 90 cm including cracking the sidewalks and streets, if any.
2. Laying down and connecting plastic pipes and then wrapping the pipe with clean soil.
3. Backfilling of the trenches by used excavated soil at a height of (0.55 m), rehabilitation and restoration of sidewalks and streets (if any) that were demolished and returned as it was with the removal of excess construction wastes.

As per design of the water distribution network, these pipes will be installed within the right of way and side walk of streets inside residential areas of each village. It is not expected that these pipes will pass through agricultural/private lands and/or cause any restriction of access and livelihood impacts.

The work will also comprise of some civil works such as excavation, lifting the soils and other waste produced during the excavation and also casting in some cases and as follows:

- Providing workers and all the surveying equipment required for the execution works.
- Conduct excavation work according to the dimensions and methodologies mentioned in the drawings with other considering the possibility of groundwater.
- Prepare all materials for the implementation of the work (pipes and joints) then wrapping them with soil.

The anticipated duration of upgrading works is about 180 days with about 15-20 workers per day with about 95% of them are local workers and the rest are engineers and technicians that may be from the closest area.

2.3 Contractors Camp and Storage of Equipment

The upgrading works will imply the setup of camps in the area near each water network if needed. The setup of camps will be established on vacant state-owned lands for storage of equipment and construction materials. The work activities will need about 15-20 local workers per day for each site. If there are non-local workers, these workers will need to have their accommodation facilities in the camp, during the construction phase.

3. BASELINE CONDITIONS

3.1 The Project Area

The subproject is located in the governorate of Al-Muthanna that is situated in southern part of Iraq, Al-Muthanna borders Saudi Arabia and shares internal boundaries with the governorates of Basra, Thi-Qar, Al-Qadisiyah, and Al-Najaf (as shown in figure 2 below). The proposed location of these water distribution networks will be in an open area.

The population in each village is shown in the table below:

Table 2: Information about the villages

No.	Village	Population
1	Abu Kanbara	1924
2	Abu Sarifah	1153
3	Al Aksheh	1173
4	Al Thawiher	1220
5	Finjan Al Thaher	850
6	Al Tawawreh	1534



Figure 2 Map of Iraq on the right and Al-Muthanna governorate on the left.

These subprojects are located in flat areas. The area adjacent to the project sites is characterized as rural residential and semi desertic to agricultural in some area.

3.2 Environmental and Social Baseline Conditions

The environmental baseline section is presented to give clear overview of the environmental and social conditions in the vicinity of the subproject location prior to commencement of works.

3.2.1 Climate

Al-Muthanna governorate is located in the southern part of Iraq. The governorate's landscape is dominated by desert plains, with only a narrow ribbon of irrigated farmland along the Euphrates River in the north. The major rain falls during the period December thru March, with a spread showering in April. During the year, about 106 mm of precipitation falls annually. In summer temperatures easily surpass 40°C, the average annual temperature is 23.8 °C. The driest weather is in June, July & August, September when no rainfall (precipitation) occurs. While, the wettest weather is in December - March when rainfall (precipitation) occurs. The average monthly wind velocity is 2.3m/s.

3.2.2 Air Quality

The subproject sites are located in open areas, so the expected concentration of air pollutants is low. Air pollutants in the villages are caused mainly from movement of vehicles and trucks. Therefore, the ambient air quality is expected to be within the WHO ambient air quality standards.

3.2.3 Site Topography and location

No natural land obstacles are presented in the subproject areas. The subproject areas are free of mountains, cliffs, and valleys. There are no protected areas or endangered species (there is no critical or high biodiversity values that might be affected) in the vicinity of the sites (more than 4 Km).

3.2.4 Land use

The area adjacent to the project sites is characterized as rural residential and semi desertic to agricultural in some area. However, the rehabilitation activities will not cause an impact on agricultural are or make any crop damage.

3.2.5 Flooding

There are no records of flooding that occurred previously in the area.

3.2.6 Noise

Currently, there is no traffic congestion and consequently the existed noise level is within the normal levels.

3.2.7 Heritage Environment

There are no sites of historical or cultural importance in the area. There are no cemeteries, historical-cultural monuments, churches, mosques near the project that need to be removed or will be impacted due to the rehabilitation activities.

3.2.8 Traffic Level

No traffic problem or traffic congestion will be expected during the construction phase or in the operation phase.

3.2.9 Land acquisition

The existing water distribution networks are built on state land and hence there are no issues related to land acquisition. The implementation activities will not cause relocation of people and any individuals.

3.2.10 Social Aspects

The suggested path for the installation of the water distribution network will be on state land, where no land or property expropriation will be necessary. All the areas around the sites remain clear of any settlement or economic use and are ready for construction works, no interference is registered from the local community which is eager for the works to be completed. It is important to mention that during the implementation of the network, it is not expected to cause restriction of access or livelihood impacts as contractor will backfill the trench directly for safety purposes as well.

4. LEGAL ASPECTS

4.1 Iraqi environmental legislations

During rehabilitation and operation phases of the project, the work must follow the Iraqi laws and regulations for the environmental standards. These are:

1. Laws of the environment protection No.3 issued in 1997 and its relevant published regulations. No environmental regulations for gaseous emissions, noise and other air pollution standards are in force and legally binding. However, limits for water disposal in any surface waters and main sewers are regulated according to the regulations no. (25)/1967 and their update modifications released from the Ministry of Health (MOH) and the Ministry of Environment.
2. New environmental framework Law No. 27 of 2009 by the Iraqi National Government was introduced but the executive decrees remain to be prepared. There are as yet no formally adopted requirements for environmental assessment.
3. Regulations governing contact with archaeological sites extend also to encompass developmental activities like road construction and rehabilitation wherever these developmental activities lie within archaeological vicinity.

4. Regulations of the MOE on sanitary waste must be followed, and for the rubbles (construction & demolition waste) the regulations, legislations and instruction of both MOHE and MOCHPM.

Table 3: Applicable Laws and Regulations in Iraq

Law	Subject
Law no. 37 of 2008 for Ministry of Environment	Describes institutional arrangements of the Ministry of Environment and Outlines policies and roles and responsibilities toward protecting the environment.
Law no. 27 of 2009	Protection and Improvement of Environment Environmental protection from pollution resulted from petrol and natural gas extraction
Regulations no. 2 of 2001	Preserving water resources.
Law no. (55) Issued in 2002	Law of heritage and antiques
Law No. 37 of 2015.	Labor Law No. 37 of 2015.

For legal aspects, the work during construction and operation must follow the Iraqi laws and regulations for the Environmental Standards. These are laws of the environment protection No.3 issued in 1997 and the published regulations. No environmental regulations for gaseous emissions, noise and other air pollution standards are in force and legally binding. However, limits for water disposal in any surface waters and main sewers are regulated according to the regulations no. (25)/1967 and their update modifications released from the ministry of health and the ministry of the environment. Law of heritage and antiques no. (55) Issued in 2002, while for a sanitary waste (municipal) the regulations of the MOE must be followed, and for the rubbles (construction & demolition waste) the regulations, legislations and instruction of both MOHE and MOCHPM must be followed. It is important also to mention that, the contractor will sign employment agreement with all construction workers by following labor law of Iraq.

It should be noted that legislation relating to social safeguards issued in Iraq since 2003 has focused primarily on the ratification of international conventions and protocols on issues such as cultural heritage. As yet there are no formally adopted requirements for social assessments relating to road works. Hence, social safeguards issues remain very largely uncovered except to the extent they are referred to under environmental laws.

4.2 The World Bank Safeguards Policies

In addition to the Iraqi laws and regulation the ESMP follows key policies and procedures of the World Bank; the following section presents the WB operational policies relevant to the rehabilitation and reconstruction of the water distribution networks.

- ❖ OP/BP 4.01 Environmental Assessment.
- ❖ OP/BP4.12 Involuntary Resettlement
- ❖ OP/BP 4.11 Physical Cultural Resources

4.3 WBG EHS: The Environmental, Health, and Safety (EHS) Guidelines

These are technical reference documents with general and industry-specific examples of Good International Industry Practice (GIIP). When one or more members of the WB Group are involved in a project, these EHS Guidelines are applied as required by their respective policies and standards.

5. IMPACT ASSESSMENT AND MITIGATION MEASURES

5.1 Construction Phase

This section of the report describes the environmental and social impacts that are likely to result from the installation of the network, and the mitigation measures addressing them. The Environmental actions, procedures and responsibilities as required during the construction phase must comply with the available specifications, legislation, laws issued by the MOHE.

The construction contractor(s) will be responsible for compliance with the ESMP provisions during the construction phase of the subprojects. The contractor will be also in charge of undertaking construction works in a manner which complies with all relevant environmental procedures, adheres to all legislative requirements, and ensures that all environmental objectives associated with the contract are achieved. The overall assessment of the key environmental and social impacts is summarized below. According to the above environmental baseline and mitigation measures, it can be expected that the significant impact is low for most of the environmental receptors due to the minimum concentrations (as a background) for some parameters and medium impact for air quality, noise and child labor while health and safety has a high impact due to the fact this issue is related directly with the health and safety for the workers and staff as shown in the table below:

Table 4: Summary of Impact Assessment during Construction

	Environmental Receptor	Impact Significance
1	Air Quality	Medium
2	Noise	Medium
3	Water Resources	Low
4	Soil	Low
5	Solid and hazardous wastes	Low
6	Flora & Fauna	Not significant
7	Topography and landforms	Not significant
8	Impacts on local traffic	Not significant
9	Health and Safety	High
10	Socio-Economic impacts	Low
11	Child Labor	Medium

5.2 Operational Phase

During the operational period, the project is expected to result in positive socio-economic outcomes for the local communities. Socially harmful consequences of

road operation are not anticipated. However, the continued operation of a GRM for one year following opening of the water network for use will ensure that local community members have an accessible, fair and transparent means of reporting any emerging adverse impacts, and a means of obtaining mitigation.

6. ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN

In this section, the identified mitigation measures will be summarized. The responsibility for implementation of the mitigation measures will be mostly upon the contractor. However, the supervision and assurance that the mitigation measures are implemented will be the responsibility of the Resident Engineer who represents the ministry as the Project Owner.

The Resident Engineer (RE) will be assisted by a team of environmental and social officers who will be responsible for supervising the daily activities of the contractor and will report non-compliances to the Resident Engineer in order to take necessary actions towards the contractor in addition to the OHS aspects. Regular supervision site visits will also be conducted by the PMO environmental/social officer in association with a qualified environmental and social consultant who will provide technical advice in case there is a need to modify or add new mitigation measures as work necessitates.

The costs of mitigation measures are estimated based on the average market rates for similar activities in Iraq and can be used as indicative costs. It is the sole responsibility of the contractor to estimate the costs associated with the recommended mitigation measures based on his work experience.

In terms of hazardous waste, the following mitigation should be followed:

- Provide adequate sanitation facilities serving all workers (mentioned in HSE).
- Paints with toxic ingredients or solvents or lead-based paints will not be used
- All waste should be deposited through licensed haulers/transporters to licensed and regulated landfill sites appropriate to the type of waste generated (e.g. solid, household, hazardous).

The following tables summarize the mitigation measures which are required to be undertaken to avoid any negative impacts on the environment. Responsibilities and estimated costs are also presented.

Table 5: Mitigation Measures during Construction Phase.

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
1	Air quality	<ul style="list-style-type: none"> • Unpaved roads, e.g. which may be utilized for construction vehicles movement or transportation of construction materials should be prepared in a way to avoid dust emissions. Watering to suppress dust should take place regularly. • Watering or increase of the moisture level of the open materials storage piles to reduce dust levels. • Enclosure or covering of inactive piles to reduce wind erosion. • Loads in all trucks transporting dust-generating materials have to be sprayed with water to suppress dust, as well as wheels of means moving inside and outside of the construction-site. • Limiting Speed for vehicles approaching the site to less than 40 km/hr. On site, speed limit should not exceed 20 km/hr. 	Contractor	Resident engineer	1000
		<ul style="list-style-type: none"> • Engines of vehicles and other machinery are kept turned on only if necessary, avoiding any unnecessary emission. • Machines and equipment are periodically checked and maintained to ensure their good working condition. • All equipment and machines must be maintained and tested for compliance with standards and technical regulations for the protection of the environment and have appropriate certifications. • Activities are carried out using the minimum required number of means at the same time. • Electric small-scale mechanization and technical tools are used when available and feasible. 	Contractor	Resident engineer	Included in contractor cost
2	Noise	Construction activities are to take place within reasonable hours during the day and early evening.	Contractor	Resident engineer	Included in contractor cost

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
		<ul style="list-style-type: none"> Equipment must be kept in good working order and where appropriate fitted with silencers which are kept in good working order. Equipment to run only when necessary Positioning of the noise sources in a concealed area with respect to acoustic receptors, consistent with the needs of the construction site. 	Contractor	Resident engineer	Included in contractor cost
		Use of personal protection equipment for workers especially those who use jack hammers or near noisy engines or compressors.	Contractor	Resident engineer	1000
3	Water resources	Wastewater from the worker rest areas or construction offices should be contained in sealed containers and should be removed regularly from site by means of authorized contractors.	Contractor	Resident engineer	1000
		In case of the need to change engine oils or refuel some construction equipment, a proper maintenance workshop or shelter should be installed to ensure containment of any fuel or oil spills via provision of secondary containment, drip trays or other overflow and drip containment measures, for hazardous materials containers at connection points or other possible overflow points	Contractor	Resident engineer	1000
		<ul style="list-style-type: none"> In case of using septic tanks on site, the engineering drawings of these tanks should be presented to the Resident Engineer for approval. The wastewater in these tanks should be collected and then transported periodically to the nearest authorized wastewater treatment plant. 	Contractor	Resident engineer	Included in contractor cost
4	Soil	<ul style="list-style-type: none"> To prevent soil contamination by oil/grease spills, leakages or releases, all manipulations of oil derivatives in the process of construction and provision of the fuel to the machines should be performed with maximum care; leak proof containers should be used for storage and transportation of oil/grease and wash off from the oil/grease handling area shall be drained through drains and collected and disposed properly Construction waste and debris shall be collected on a regular basis and disposed of at designated landfills; Only authorized quarries shall be used for purchasing soil to be used for embankment, padding, bedding, backfilling during construction; and 	Contractor	Resident engineer	Included in contractor cost

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
		<ul style="list-style-type: none"> It must be prohibited to operate equipment and vehicles outside the designated work areas and roads. Reuse the excavated soil when it deemed technically appropriate. 			
		<ul style="list-style-type: none"> No hazardous waste storage to take place directly on soils. Appropriate and enclosed containers away from direct sunlight, wind and rain. Provide adequate ventilation where volatile wastes are stored. Limiting access to hazardous waste storage areas to employees who have received proper training 	Contractor	Resident engineer	1000
5	Solid and hazardous wastes	<ul style="list-style-type: none"> Minimizing hazardous waste generation by implementing stringent waste segregation to prevent the commingling of non-hazardous and hazardous waste to be managed. Provision of readily available information on chemical compatibility to employees, including labeling each container to identify its contents Limiting access to hazardous waste storage areas to employees who have received proper training Simple waste management plan for specific waste streams must be developed. Non- hazardous or municipal waste must be collected and transported to local council approved disposal sites. Food wastes must be collected, where practicable, considering health and hygiene issues, for disposal off-site through licensed contractors. Waste containers must be located at each worksite. Chemical wastes must be collected in 200 liter drums (or similar sealed container), appropriately labeled, for safe transport to an approved chemical waste depot or collection by a liquid waste treatment service. Storage, transport and handling of all chemicals must be conducted in accordance with all legislative requirements, through licensed contractors and in coordination with the local authority. All hazardous wastes must be appropriately stored in bounded areas and should be clearly identified as “hazardous”. 	Contractor	Resident engineer in coordination with the local authority and ministry of science and technology regarding hazardous wastes	1000

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
		<ul style="list-style-type: none"> • Transportation and disposal of hazardous wastes should be done through licensed contractors and in close coordination with the relevant local authority and in compliance with the legal requirements and instructions of the ministry of science and technology previously. • Hazardous liquids, such as solvents, rust proofing agents and primer must be managed in accordance with the requirements of relevant legislation and industry standards. • Material Safety Data Sheets (MSDS) for hazardous materials must be available on-site during construction and made available and explained to workers. • Hydrocarbon wastes, including lube oils, must be collected for safe transport off-site for reuse, recycling, transport or disposal at approved locations. 			
6	Flora & Fauna	Not Applicable	Not Applicable	Not Applicable	Not Applicable
7	Topography and landforms	Not Applicable	Not Applicable	Not Applicable	Not Applicable
8	Traffic	<ul style="list-style-type: none"> • Where practicable, truck deliveries must be restricted to daytime working hours. • Clear traffic signs and signs signals must be installed on-site to provide for safe traffic. 	Contractor in coordination with the Local Traffic Department for some sections	Resident Engineer	500
9	Health and Safety	<ul style="list-style-type: none"> • Limit speed of construction vehicles and provide road signage for drivers and local community. 	Contractor	Local traffic department in coordination with the Resident engineer for some sections	500

Receptor	Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
	<ul style="list-style-type: none"> • Having a clear set of OHS Plan and Procedures. • Having a detailed emergency plan including the nearest medical center and the location of the first aid kits. • Qualified personnel must be employed for the construction equipment, and personnel must be trained for health and safety issues. • Personal protection equipment such as eyeglasses, gloves, hard heads and safety belts must be supplied and continuously used by all workers, technicians, engineers and site visitors. 	Contractor	Resident engineer	1000
	<ul style="list-style-type: none"> • Testing structures for integrity prior to undertaking work; • Implementation of a fall protection program that includes training in climbing techniques and use of fall protection measures; • An approved tool bag should be used for raising or lowering tools or materials to workers on structures; • Use of helmets and other protective devices will mitigate against scratches, bruises, punctures, lacerations and head injuries due to dropping objects. • Adherence to local and international guidance and codes of practice on EHS management during construction; • management, supervision, monitoring and record-keeping; • implementation of EHS procedures as a condition of contract with contractors and their sub-contractors; • clear definition of the EHS roles and responsibilities of the companies involved in construction and to individual staff (including the nomination of EHS supervisors during construction and an EHS coordinator during operation); • pre-construction assessment of the EHS risks and hazards associated with construction and operation, including consideration of local cultural attitudes, education level of workforce and local work practices; • provision of appropriate training on EHS issues for all construction and operation workers, including initial induction and regular refresher training, taking into account local cultural issues; 	Contractor	Resident engineer	Included in contractor cost

Receptor	Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
	<ul style="list-style-type: none"> • provision of health and safety information; • regular inspection, review and recording of EHS performance; • protective systems to be put in place to protect workers from cave-in in trenches. 			
	<ul style="list-style-type: none"> • Any accidents to be reported and treated within site as a first aid procedure. • Safety training for the workers. • Fuel and oil changing shelters should be equipped with necessary firefighting and safety equipment • First aid boxes should be available all times onsite and trained staff on emergency aids should be identified. 	Contractor	Resident engineer in coordination with health and safety officials.	1000
	<ul style="list-style-type: none"> • Provide surveillance and active screening, and immunization • Provide treatment on-site or in community health care facilities • Eliminate unusable impounded water, and apply vector control programs • Erect suitable and adequate warning signage along culvert cleaning and excavation sites • Collaborate with local communities and responsible authorities to improve signage and visibility • Avoid uncovered piles of aggregates and other construction materials • Avoid burning waste in worksites • Avoid or minimize driving through community areas and dangerous routes during daytime • Alert drivers on local speed limits, and monitor implementation • Minimize traffic by purchasing from the local markets to the extent possible • Closing of trenches on the same day, • If a trench will be left open for the day after, barriers to prevent community members and unauthorized personnel will be put in place. • Assign local security personnel to prevent unauthorized entry to the site. 	Contractor	Resident engineer in coordination with health and safety officials.	1000

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
		<ul style="list-style-type: none"> Signs and awareness should be installed close to the excavation area to protect road users and community. Contractor prepares and implements Traffic Management Plan and Pedestrian Safety Plan 			
10	Handling Complaints	<ul style="list-style-type: none"> A complaints register will be kept on site and this will feed into the GRM. Details of complaints received will be incorporated into the audits as part of the monitoring process. 	Resident Engineer	PMO	Included in contractor cost
11	Cultural Heritage	<ul style="list-style-type: none"> In case of accidental discovery stop all works and contact the responsible authority within 24 hours; Provide training to the construction crew on the mode of conduct in case of accidental findings <p>Chance find procedures will be used as follows: Stop the construction activities in the area of the chance find;</p> <ul style="list-style-type: none"> Delineate the discovered site or area; Secure the site to prevent any damage or loss of removable objects. In cases of removable antiquities or sensitive remains, a night guard shall be present until the responsible local authorities and the Ministry of Culture take over; Notify the supervisory Engineer who in turn will notify the responsible local authorities and the Ministry of Culture immediately (within 24 hours or less); Responsible local authorities and the Ministry of Culture would be in charge of protecting and preserving the site before deciding on subsequent appropriate procedures. This would require a preliminary evaluation of the findings to be performed by the archeologists from the Department of Antiquities and the Ministry of Culture (within 72 hours). The significance and importance of the findings should be assessed according to the various criteria relevant to cultural heritage; those include the aesthetic, historic, scientific or research, social and economic values; Decisions on how to handle the finding shall be taken by the responsible authorities from DA and the Ministry of Culture. This could include changes in the layout (such as when finding an irremovable remain of cultural or archeological importance) conservation, preservation, restoration and salvage; Implementation for the authority decision concerning the management of the finding shall be communicated in writing by the Ministry of Culture; and 	Contractor	Resident engineer in coordination with Heritage Authority.	Included in contractor cost

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
		<ul style="list-style-type: none"> Construction work could resume only after permission is given from the responsible local authorities and the Ministry of Culture concerning safeguard of the heritage 			
12	Child labor and Gender Based Violence	<ul style="list-style-type: none"> Rigid obligations and penalties will be added to the contractor contracts in order to warrantee no child labor exist in the subproject The PMO will oblige the contractor to keep a copy of IDs of laborers in order to monitor the hired staff (Chapter 11 of the 2015 Labor Law of Iraq sets the age for hazardous works 18 years old). Labor influx should also be managed by contractor and ensure Code of Conduct is introduced and applied to avoid impact on local community and provide mitigation measure for GBV risks The contractor also will be obliged to maintain daily attendance sheets in order to verify the attendance of workers in case of accidents and provide the injured persons with proper health insurance <ul style="list-style-type: none"> The code of conduct for workers/contractors should be introduced to prevent misconducts, including prevention of sexual harassment and gender based violence and also training and awareness rising for workers should be continued, through daily toolbox talks and other training opportunities. 	Contractor	Resident engineer	Included in contractor cost
Total cost US\$ (Construction phase)					9,000

Table 6: Mitigation Measures during Operation Phase.

Receptor		Mitigation Measures	Responsibility	Supervision	Total estimated Cost in US\$
1	Air quality	<ul style="list-style-type: none"> The net impact of the Project on air quality is not applicable, and will be limited to Construction Period. 	Not Applicable	Not Applicable	Not Applicable
2	Noise	<ul style="list-style-type: none"> Not applicable 	Not Applicable	Not Applicable	Not Applicable
3	Water resources	<ul style="list-style-type: none"> Not applicable 	Not applicable	Not applicable	Not applicable
4	Soil	<ul style="list-style-type: none"> Not applicable 	Not applicable	Not applicable	Not applicable
5	Solid and hazardous wastes	<ul style="list-style-type: none"> Not applicable 	Not applicable	Not applicable	Not applicable
6	Flora & Fauna	<ul style="list-style-type: none"> Not applicable 	Not Applicable	Not Applicable	Not Applicable
7	Topography and landforms	<ul style="list-style-type: none"> Not Applicable 	Not Applicable	Not Applicable	Not Applicable
8	Handling Complain	<ul style="list-style-type: none"> The continued operation of a GRM for one year following operating of the network for use will ensure that local community members have an accessible, fair and transparent means of reporting any emerging adverse impacts, and a means of obtaining mitigation. 	Local authorities	Local authorities	No cost
9	Health and Safety	<ul style="list-style-type: none"> Having a clear set of OHS Plan and Procedures. Provision of health and safety information; Regular inspection, review and recording of EHS performance; 	Contractor	Resident engineer	Included in contractor cost
Total cost US\$ (Operation phase)					No Cost

7. ENVIRONMENTAL AND SOCIAL MONITORING PLAN

7.1 Environmental and Social Monitoring

In order to ensure full compliance of the performed activities to the environmental and social requirements, regular monitoring should be performed. For this purpose, an environmental and social monitoring program has been established for the construction phase to ensure the proper implementation of the environmental and social mitigation measures.

7.2 ESMP Institutional Arrangements

In order to ensure full compliance with the environmental and social requirements which are described above, PMO nominated a qualified engineer to act as the focal point for environmental and social affairs at the central level. On the field level, PMO nominated two engineers in Al-Muthanna to act as environmental and social officers. Those engineers will be trained on monitoring and reporting of environmental and social impacts and how to fill the checklist to be used during field visits before implementation starts.

The Resident Engineer will be the officially responsible staff member for ensuring environmental and social compliance. S/He will be assisted by the designated environmental and social field officers.

In addition, a qualified consultant is recruited by the PMO to provide technical assistance and capacity building to the environmental and social team both at the central level and at the field level.

7.3 Reporting requirements

In order to ensure that the mitigation and monitoring measures are being carried out effectively with the required frequency, a clearly defined and regular reporting and response system must be established. The needed frequency of report generation for inspection is to be monthly, and for auditing twice a year, environmental monitoring is once per year.

The information will be made available to the relevant regulatory authorities as required. In addition to the monitoring and reporting requirements documented in the relevant sections of the ESMP, the following reporting regime will be implemented:

- a) All incidents or accidents during the rehabilitation should be reported immediately to relevant authorities.
- b) All corrective measures must be discussed to ensure compliance with laws and regulations.
- c) Reports for personnel training on environmental issues or emergency practices must be produced.
- d) Progress reports, environmental monitoring report and other inspections reports must be produced periodically.

The PMO environmental and social field officers will provide the Resident Engineer with a weekly report briefing their observations and recommendations for action. Whereas the Resident Engineer shall prepare an environmental and social management report on monthly basis to PMO in Baghdad.

Table 7: Monitoring Activities during Construction Phase.

Receptor		Monitoring Activities	Monitoring Indicators	Frequency	Responsibility	Supervision	Total estimated Cost in US\$
1	Air quality	<ul style="list-style-type: none"> Investigate dust complaints from workers and residents Visual inspection of vehicles and equipment operating or entering the site and Measurements of exhaust emissions (CO, SO_x, NO_x, PM₁₀, PM_{2.5}) 	<ul style="list-style-type: none"> Recorded and documented complaints Record the status of equipment and vehicles on site (excessive black or white smoke) 	<ul style="list-style-type: none"> Daily visual inspection Once every six month 	Resident Engineer	PMO	1,000
2	Noise	Investigate noise complaints from workers and neighboring communities in the affected locations	<ul style="list-style-type: none"> Recorded and documented complaints Recorded tests results 	<ul style="list-style-type: none"> Weekly inspection of complaints Only in case of complains 	Resident Engineer	PMO	1,000
3	Water resources	<ul style="list-style-type: none"> Investigate implementation of mitigation measures and observe any oil or fuel spills. Investigate wastewater disposal measures 	Site Investigation report	Daily Investigation	Resident Engineer	PMO	No cost
4	Soil	<ul style="list-style-type: none"> Observe any soil contamination with oil or fuel Observe any accumulation of wastes 	Site Investigation report	Monthly	Resident Engineer	PMO	No cost
5	Solid and hazardous wastes	<ul style="list-style-type: none"> Maintain records on waste types and quantities Observe any waste accumulation in un approved locations 	<ul style="list-style-type: none"> Waste management contracts with authorized contractors Waste delivery receipts from local authorities. 	<ul style="list-style-type: none"> Weekly Weekly 	Resident Engineer	PMO	No cost

Receptor		Monitoring Activities	Monitoring Indicators	Frequency	Responsibility	Supervision	Total estimated Cost in US\$
6	Health and safety	<ul style="list-style-type: none"> Ensure compliance of workers to Health and Safety requirements Maintain log on incidents and accidents 	Observation report Accidents report	Weekly	Resident Engineer	PMO	No cost
7	Flora & Fauna	Record any observation about wild animals or plants on site or nearby and report to the Environmental Authority	Observation report	Upon occurrence	Resident Engineer	PMO	No cost
8	Topography and landforms	No monitoring required	Not applicable	Not applicable	Not applicable	Not applicable	Not applicable
9	Traffic	Ensure speed limits and warning signs are installed	Road signs are installed.	Monthly	Resident Engineer	PMO	No cost
10	Handling Complaints	Ensure that the GRM is effective and well communicated	Number of complaints received, analyzed and responded to.	Weekly	Resident Engineer	PMO	No cost
11	Child labor and Gender Based Violence	<ul style="list-style-type: none"> Ensuring that children and minors are not employed directly or indirectly on the project. Ensure to prevent misconducts, including prevention of sexual harassment and gender based violence. 	<ul style="list-style-type: none"> A copy of IDs of laborers and labor registry. Percentage of workers that have attended the code of conduct training and number of GBV training delivered. 	<ul style="list-style-type: none"> Daily Weekly 	Resident Engineer	PMO	No cost
Total cost US\$ (Operation/Maintenance phase)							2,000

The environmental and social consultant will prepare a monthly environmental and social supervision report after conducting site supervision visits.

On quarterly basis, PMO shall prepare an environmental and social progress report which will be submitted to the international financial institution (WB) for review and disclosure.

7.4 Capacity Development and Resources Requirements

PMO dedicated sufficient human resources to undertake the environmental and social management requirements as explained above. The assigned staff at the central and field levels are competent in the field of engineering and have variable practical experience. For the staff who will be responsible for undertaking the environmental and social tasks, they will require some capacity development.

All construction personnel and contractors are required to undertake appropriate environmental training and induction programs including, importantly, on GRM procedures.

All managers and supervisors will be responsible for ensuring that personnel under their control have the requisite competencies, skill and training to carry out their assigned tasks in accordance with the requirements of the ESMP. They will also be responsible for identifying additional training and competency requirements.

All project supervisors and managers will receive additional detailed training on the use and implementation of the ESMP. The following Table presents the proposed institutional strengthening program and capacity development requirements.

Table 8: Capacity Development Requirements

Capacity development topic		Provider(s)	Duration	Estimated Cost (US\$)
1	Environmental Impact Assessment Environmental and social Management in Construction Sites	Consultant	3 Days	1,500
2	Iraqi Environmental Legal Requirements	Ministry of Environment	1 Day	500
3	World Bank Environmental and Social Safeguards	Consultant	2 Days	1,000
Total Estimated Cost				\$3,000

In order to ensure full compliance of the environmental and social requirements, regular site visits should be conducted. Dedicated office spaces, office equipment and supplies in addition to adequate means of transportation should be made available for the environmental and social management team at the central level and most importantly on the field level. MOP PMO should ensure the allocation of sufficient budget resources to ensure availing the required resources to achieve the required tasks.

8. PUBLIC CONSULTATION

8.1 Consultation Process:

The public consultations were carried out in the six villages for Rehabilitation of water distribution networks on 12 and 13 of October, 2019. The public consultations included only men and number of participants was 64 in these villages. Accordingly, a questionnaire was formatted to cover the key environmental and social aspects related to the subproject. The consultation started by providing briefs about the subproject activities, potential impacts and future benefits.

In addition to public consultation, one on one interviews were conducted on 12 and 13 of October, 2019. The formatted questionnaire was then addressed to 8 women and 30 men in the surrounding community randomly to have their opinions and thoughts regarding the construction activities.

8.2 Consultation Results:

All participants in these villages expressed that; the upgrade of these water network will have a positive impact on their social daily life. Please refer to Annex 2 and Annex 3 for sample of public consultations in Al Thawiher village and also sample of individual interviews for both men and women. The full list of participants for public consultations and individual interviews are attached in standalone document to reduce the size of the instrument. As per the questionnaire prepared for individual interview, the below are the main findings:

- 1) All interviewed locals agreed that the rehabilitation activities of water distribution networks will serve all the people in the village and have a strong positive impact from the social perspectives on the locals.
- 2) No claims from any locals were recorded or alleged regarding the ownership of the land were the water distribution networks are constructed; all agreed that is governmental land property.
- 3) The project will contribute to strength the health awareness by avoiding the purchase of potable water which might be not sterilized properly specially in the summer.
- 4) The rehabilitation of the project will enhance the economic situation of the people via avoiding the purchase of extra water to cover their daily requirements.
- 5) They welcomed that there will be a hot line to express their suggestion or concern that might happen during the rehabilitation phase.
- 6) No vegetation covers, crops, plants, trees...etc. will be removed in order to execute the rehabilitation activities of the water distribution networks.
- 7) The interests of the locals will not be affected in any way by the rehabilitation activities.
- 8) No infrastructure within the water distribution network area will be affected negatively due the rehabilitation activities and there is no need for alternative roads.
- 9) No deportation, dislocation of any of the local community will be needed due to these activities.
- 10) As long as there are some excavation activities, the locals asked to take the proper precaution mitigations to avoid any accident that might happen.

- 11) The rehabilitation of the project will enhance the social relationship among the locals; improve their achievements and performance via the availability of Water.

9. GRIEVANCE REDRESS MECHANISM

The SFD is in the process of establishing a free hotline and is expected to be functioning within the next few months. SFD is planning to set up a digital system with multi-channels for receiving complaints, inquiries, feedbacks or comments like WhatsApp, Facebook, email and complain boxes for each subproject. Additionally, focal points will be assigned at local level and central level to be in charge of handling complaints.

Meanwhile, in order to comply with the WB requirements, SFD has temporarily assigned three staffs as focal points with their cell phone numbers to be disseminated at each subproject level for receiving calls and handling complaints. The contact details will be posted at subproject signboard and the complaint boxes will be installed in each location as shown in the below table.

Table 9: Contact Information for GRM

#	Name	Job Title	Phone Number	E-mail
1	Kabil Hmood Abas	SFD Team leader	07812542417	Muth_planning@yahoo.com
2	Mohammed Thamer Fitan	GRM officer	07803008372	Muth_planning@yahoo.com
3	Yaser Mohammed Sehood	M&E officer	07812542417	Muth_planning@yahoo.com

The process of managing complaints will be as follows:

- 1- Complaints should be sorted out according to complexity;
- 2- Simple inquiries should be resolved on the spot by concerned staff members in 3-6 working days as a maximum and should be documented and archived as per the relevant procedure;
- 3- Complex issues should be investigated and communicated with higher management for final decisions within a timeframe of 20 working days as a maximum;
- 4- After the completion of the proceedings, the complaint is closed, and information is included in the system, including the action(s) taken and the result(s) required; and
- 5- The complainant shall be notified of the result and the action immediately and informed of the possibility of objecting to the procedure.

In addition to PMO, the MOP, project offices in governorates, and Community Development Groups (CDGs), the World Bank's Grievance Redress System (GRS) can also be approached for reporting and resolving issues.

ANNEXES

Annex 1: Public Consultations Photos



Public Consultations at Al Thawihher Village



Public Consultations at Finjan Al Thaher Village



Public Consultations at Al Aksheh Village



Public Consultations at Abu Sarifah Village



Public Consultations at Abu Kanbara Village








Public Consultations at Al Tawawreh Village












Annex (2): Sample of Public Consultation at these six Villages

تقرير فريق الإجراءات البيئية والاجتماعية
<p>محافظة المنيا / قرية ال ظويهر</p> <p>مشروع (تجهيز ومد شبكة في منطقة ال ظويهر في الهلال)</p> <p>وصف المشروع : تجهيز مواد واجور عمل القيام بتجهيز انابيب بلاستيك قطر 160 ملم بطول 750 م و 110 ملم بطول 700 م شاملا السعر القيام بالحفر بالعمق المطلوب مع وضع طبقة من الرمل النهري سمك 30 سم اسفل واعلى الابواب مع دفن الابواب والملحقات بالتراب الثقيل الخالي من الشوائب وربط الابواب شاملا السعر القيام بالحفر ومد وكبس وربط والحصى الهيدروليكي ودفن الانابيب وكل ما يتطلبه العمل من اجور ومواد .</p> <p>محضر اجتماع المشروع</p> <p>1. تم اعداد الكشوفات من قبل اللجنة المختصة و المشكلة في الصندوق الاجتماعي للتنمية وبإشراف اللجنة المجتمعية في القرية علما ان المشروع هو اولوية القرية الثالثة</p> <p>2. ان المشروع سيساهم في تحسين الواقع الاجتماعي والاقتصادي للقرية من خلال توفير المياه الصالحة للشرب لمنطقة واسعة من القرية وتقليل الاخطار الناتجة عن تجهيز الماء من خلال سيارات متنقلة .</p> <p>3. لا يوجد تعارضات أو تجاوزات على أرض المشروع وكذلك ان المشروع لا يحتاج الى استملاكات أو تعويضات حيث يقع المشروع على محرم الشارع العام و هي مخصصة للتفيع العام.</p> <p>4. ان المشروع يخدم شريحة كبيرة من سكان القرية .</p> <p>5. اكدت اللجنة المجتمعية ان المشروع لا يحتاج الى انشاء طرق بديلة حيث ان المشروع لا يؤدي الى قطع الطرق الحالية .</p> <p>6. لا يؤثر المشروع على الحياة البرية او البيئة الحيوية المحيطة بموقع المشروع وكذلك لا يؤدي الى قطع الاشجار او رفع المزروعات و لا يؤدي الى تغيير ديموغرافية المنطقة، رغم ذلك نؤكد على ضرورة الالتزام بجميع الاجراءات الوقائية البيئية اتناء تنفيذ المشروع .</p> <p>7. رحبت اللجنة المجتمعية للقرية بوجود خط سائق للمشروع مع الإدارة التنفيذية للصندوق في حال حصول اي عارض.</p> <p>8. المشروع لا يؤثر على الحياة الاقتصادية للمنطقة حيث لا توجد بالقرب من المشروع اي اصناف تجارية .</p> <p>9. ان المشروع سيساهم في تحسين الواقع الاقتصادي للقرية من خلال توفير المياه الصالحة للشرب وتقليل الاعباء المالية الناجمة عن شراء الماء بأسعار عالية مقارنة مع دخل الفرد هناك .</p>

<p>10. ليس للمشروع اي اثار اجتماعية سلبية بل العكس فان المشروع سيؤدي الى تقليل المشاكل الاجتماعية الناتجة عن انقطاع الماء و قلة التجهيز والذي سيؤدي الى زيادة التماسك و الترابط الاجتماعي .</p> <p>11. اكدت اللجنة المجتمعية على دعمها الكامل للمشروع وتقديم اي مساعدة ممكنة للقائمين على المشروع اتناء تنفيذه .</p> <p>12. اكدت اللجنة المجتمعية ان المشروع لا يؤدي الى اعادة توطين لشخص او الاضرار باي مواطن بل العكس .</p> <p>13. المشروع سيساهم في تعزيز الجانب الصحي أيضاً وذلك من خلال تجنب شراء الماء غير المعقم و غيرها من مردودات صحية بهذا الخصوص.</p> <p>14. يشمل المشروع اعمال حفر لنا نؤكد على ضرورة اتخاذ جميع الاجراءات الوقائية البيئية المخصصة لهكذا نوع من المشاريع خدمة لاهالي القرية .</p> <p>15. تم مناقشة اهالي القرية بجميع تفاصيل العمل بالمشروع و الاجابة عن كافة اسئلتهم و استفساراتهم اضافة الى الاستعلام منهم عن المشاكل التي تعاني منها القرية و بين الاهالي ان المشروع سيساعد على ايجاد الحل الناجح لحدى اهم مشاكل القرية</p> <p>16. نرفق طياً صور لمنطقة المشروع واللجنة المجتمعية مطبوعة على (CD)</p> <p>17. نرفق طياً استمارات الاستبيان للمشروع عدد (6)</p>				
<table border="1"> <thead> <tr> <th>خط العرض</th> <th>خط الطول</th> </tr> </thead> <tbody> <tr> <td>31.27'48.12"N</td> <td>45.7'58.91"E</td> </tr> </tbody> </table>	خط العرض	خط الطول	31.27'48.12"N	45.7'58.91"E
خط العرض	خط الطول			
31.27'48.12"N	45.7'58.91"E			

الترتيب	الاسم	التوقيع
١-	تارسي حاسم / حصة البنية المنهجية	
٢-	حاسم حسان / حصة بنية	
٣-	احسان عبد حميد / حصة بنية	
٤-	حميد عبد عزيز / حصة بنية	
٥-	ربيعان عبد علي / حصة بنية	
٦-	تارسي حفيد / حصة بنية	
٧-	صهبا د علي حاسم / حصة بنية	
٨-	عبد الكاشم حادي / حصة بنية	
٩-	علي شموي حمود	
١٠-	مشاق حكاظم حادي	
١١-	حاسم طاب عبد	

التوقيع	الاسم	التسلسل
	محمد عبدالرفيع / نائب رئيس اللجنة	١
	عبيد بيده / رئيس اللجنة	٢
	عادل بيده / عضو	٣
	عتق جميل / عضو	٤
	هانى مهري / عضو	٥
	شادي صعيد / عضو	٦
	محمد شادي / عضو	٧

التوقيع	الاسم	التسلسل
	كريم شادي / نائب رئيس اللجنة	١
	عتق جميل / نائب رئيس اللجنة	٢
	نصار ماضي / عضو اللجنة	٣
	حسن عجمه عباس / عضو اللجنة	٤
	وافيق عبدالله / عضو اللجنة	٥
	هانى هاجم / عضو اللجنة	٦
	هانى حيار / عضو اللجنة	٧
	هانى زهران / عضو اللجنة	٨
	هانى شادي / عضو	٩
	هانى شادي / عضو	١٠
	هانى شادي / عضو	١١

التوقيع	الاسم	التسلسل
	هانى شادي / عضو	١
	هانى شادي / عضو	٢
	هانى شادي / عضو	٣
	هانى شادي / عضو	٤
	هانى شادي / عضو	٥
	هانى شادي / عضو	٦
	هانى شادي / عضو	٧
	هانى شادي / عضو	٨
	هانى شادي / عضو	٩
	هانى شادي / عضو	١٠
	هانى شادي / عضو	١١

التوقيع	الاسم	التسلسل
	سلام عبد الزهره / رئيس اللجنة	1-
	عقيل حسن / عضو اللجنة	2-
	رياض حمزة / عضو اللجنة	3-
	هادي عبد حمزة	4-
	هادي نايف	5-
	راضي عصيه	6-
	هادي داخل / عضو اللجنة	7-
	جابر عبد الوهيد / عضو اللجنة	8-
	ناصر حسين / عضو اللجنة	9-
	هادي عبد الحسن / عضو اللجنة	10-
	قاسم كطيف	11-
	احمد حسن الحسن / عضو اللجنة	12-
	هادي عطيه قصير	13-

التوقيع	الاسم	التسلسل
	سلام عبد الزهره / عضو اللجنة	1-
	هادي ابراهيم فتوي / عضو اللجنة	2-
	هادي فتوي / عضو اللجنة	3-
	هادي سليمان جيل	4-
	هادي بجاي عبد / عضو اللجنة	5-
	هادي حسن عبد / عضو اللجنة	6-
	هادي سلطان جيل / عضو اللجنة	7-
	هادي احمد فتويان / عضو اللجنة	8-
	هادي مشيت فتاله	9-
	هادي فتويان فتاله / عضو	10-
	هادي علوي علوي عبد / عضو	11-

Annex (3): Sample individual interviews for both men and women

(استبيان)

اسم المشروع: **الرياح المائية قرب الطوارنة**
 الاسم: **ماجدة تاجية عبيدات**
 الجنس: ذكر أنثى
 المهنة: **ربة بيت**

السؤال	نعم	لا	الملاحظات
هل تعتقد ان عملية اصمار المشروع لها اثر ايجابية من الناحية الاجتماعية بالنسبة للسكان القاطنين في المناطق القريبة من المشروع	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك ادعاءات او مطالبات من قبل السكان المحليين بعائدية الارض المقام عليها المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
بسبب اصمار الاثمار ، هل هناك عمليات رفع لمحاصيل زراعية او اشجار او اي غطاء نباتي تعود عائديته لمواطنين او السكان المحليين؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تضررت مصالح المواطنين القاطنين بالقرب من المشروع بسبب اصمار الاثمار؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك اي بنى تحتية دائمية او مؤقتة تلعب دورا اساسيا في النشاطات الحيوية اليومية للسكان مستأثر بعملية اصمار المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل ان اصمار اشجار المشروع مستسبب باجراءات اعادة توطين لشخص او لاشخاص الى مناطق جديدة؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تمت عملية استخدام ارض المشروع من قبل السكان المحليين، علما ان الارض تابعة للدولة؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تتوقع وجود تاثيرات اجتماعية سلبية بالمنطقة نتيجة اصمار المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك تغيير ديموغرافي او ضرر في الصيغ الاجتماعي نتيجة عمليات الاصمار؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل يحتاج المواطنون القريبون من المشروع لوضع علامات تحذيرية او استدالات لزيادة معدلات الامان؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

التوقيع: **ماجدة تاجية عبيدات**
 الاسم: **ماجدة تاجية عبيدات**
 التاريخ: **2019 / 1**

(استبيان)

اسم المشروع: **تجيز رمد ستيك مار / قرية ان فومر**
 الاسم: **محمود**
 الجنس: أنثى ذكر
 المهنة: **مستاعد**

السؤال	نعم	لا	الملاحظات
هل تعتقد ان عملية اصمار المشروع لها اثر ايجابية من الناحية الاجتماعية بالنسبة للسكان القاطنين في المناطق القريبة من المشروع	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك ادعاءات او مطالبات من قبل السكان المحليين بعائدية الارض المقام عليها المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
بسبب اصمار الاثمار ، هل هناك عمليات رفع لمحاصيل زراعية او اشجار او اي غطاء نباتي تعود عائديته لمواطنين او السكان المحليين؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تضررت مصالح المواطنين القاطنين بالقرب من المشروع بسبب اصمار الاثمار؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك اي بنى تحتية دائمية او مؤقتة تلعب دورا اساسيا في النشاطات الحيوية اليومية للسكان مستأثر بعملية اصمار المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل ان اصمار اشجار المشروع مستسبب باجراءات اعادة توطين لشخص او لاشخاص الى مناطق جديدة؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تمت عملية استخدام ارض المشروع من قبل السكان المحليين، علما ان الارض تابعة للدولة؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل تتوقع وجود تاثيرات اجتماعية سلبية بالمنطقة نتيجة اصمار المشروع؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل هناك تغيير ديموغرافي او ضرر في الصيغ الاجتماعي نتيجة عمليات الاصمار؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
هل يحتاج المواطنون القريبون من المشروع لوضع علامات تحذيرية او استدالات لزيادة معدلات الامان؟	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

التوقيع: **محمود حسن**
 الاسم: **محمود حسن**
 التاريخ: **2019 / 1**
